



PROJECT WIDE						
PROJECT WIDE						
1000	20	0	3	11JUL07A	30JUL07A	
1120	3	0	1	07SEP07A	07SEP07A	
1060	1	0	1	11SEP07A	11SEP07A	
1090	31	0	1	31JUL07A	13SEP07A	
1010	2	0	2	13SEP07A	14SEP07A	
1200	7	0	1	27SEP07A	27SEP07A	
1220	7	0	1	27SEP07A	27SEP07A	
1110	10	0	1	17SEP07A	28SEP07A	
1180	10	0	1	01OCT07A	05OCT07A	
1210	8	0	3	28SEP07A	16OCT07A	
1230	8	0	3	28SEP07A	16OCT07A	
1140	5	5	1	14SEP07A	25OCT07	2
1130	10	8	3	08SEP07A	26OCT07	4
1050	10	10	1	01OCT07A	01NOV07	2
1150	10	10	1	17SEP07A	01NOV07	2
1080	19	19	1	10OCT07A	15NOV07	2
1190	20	20	1	13SEP07A	16NOV07	177
1020	30	30	3	17NOV07	16DEC07	262
1030	30	30	2	23NOV07	28DEC07	233
1040	30	30	2	17DEC07	22JAN08	223
1240	30	30	2	17DEC07	22JAN08	223
9000	0	0	3		24JUN09	0
9020	15	15	1	04JUN09	24JUN09	0
1100	700	657	3	13SEP07A	05AUG09	8
9010	0	0	3		05AUG09	0
9030	30	30	1	25JUN09	05AUG09	0

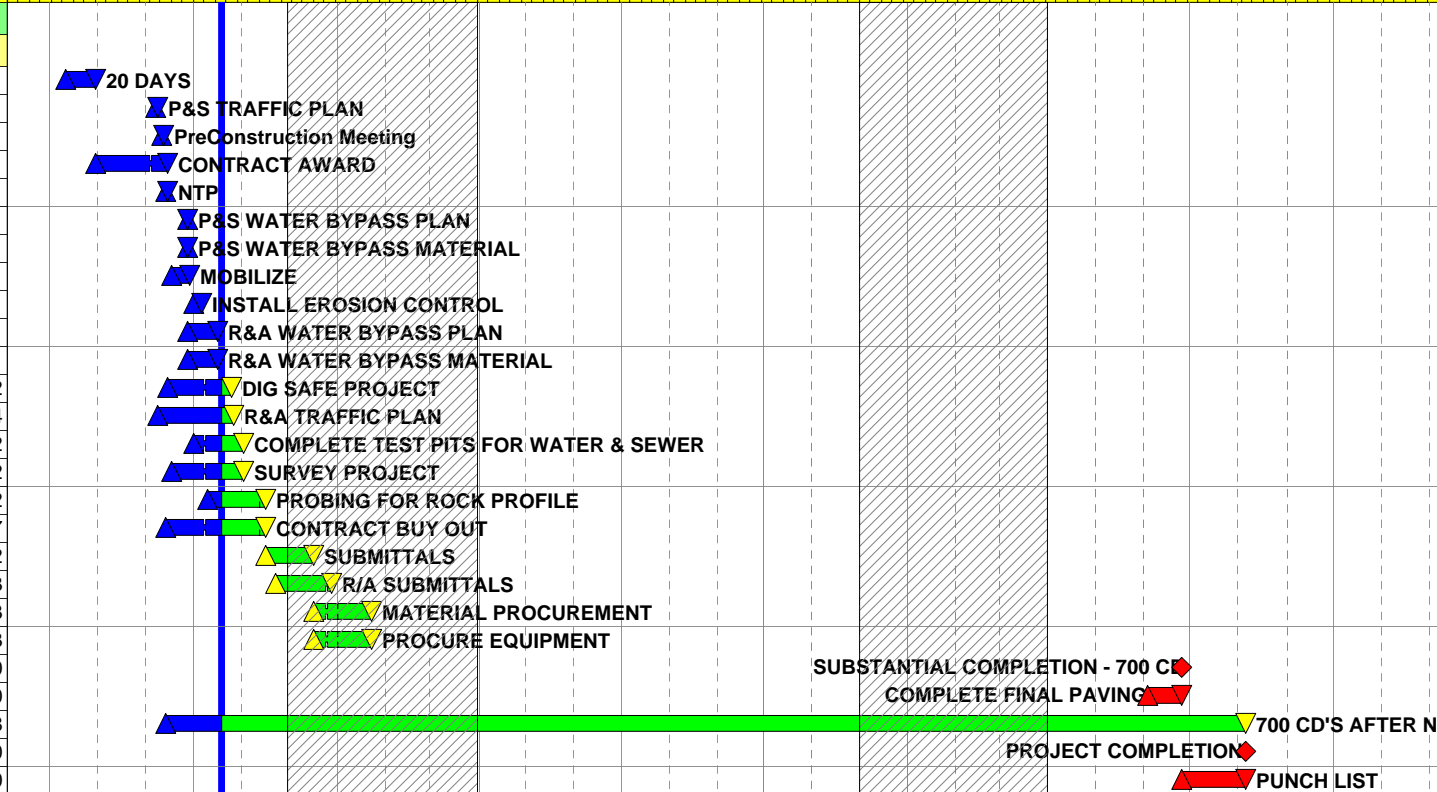

AREA 1 - YELLOW						
CREW 1						
2220	5	8	1	09OCT07A	30OCT07	2
2000	7	7	1	31OCT07	08NOV07	2
2010	4	4	1	09NOV07	15NOV07	166
2020	10	10	1	16NOV07	03DEC07	166
2040	2	2	1	04DEC07	05DEC07	166
2030	10	10	1	06DEC07	19DEC07	166
2410	8	8	1	20DEC07	04JAN08	166
2420	2	2	1	07JAN08	08JAN08	171
2430	4	4	1	07JAN08	10JAN08	169
2590	7	7	1	07JAN08	15JAN08	166
2440	8	8	1	16JAN08	25JAN08	166
2450	2	2	1	28JAN08	29JAN08	166
2460	4	4	1	30JAN08	04FEB08	166
2465	9	9	1	05FEB08	15FEB08	166
2470	6	6	1	18FEB08	25FEB08	166
2480	2	2	1	26FEB08	27FEB08	166
2490	4	4	1	28FEB08	04MAR08	166

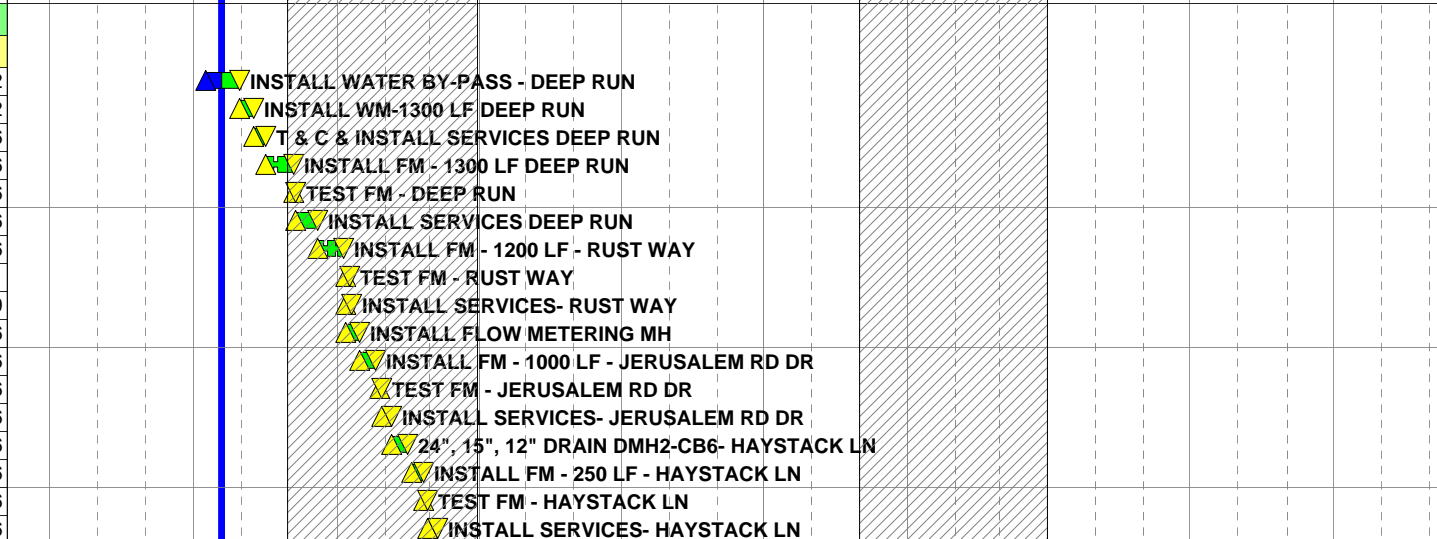

Start Date: 11JUL07
 Finish Date: 05AUG09
 Data Date: 19OCT07
 Run Date: 26OCT07 12:27

Early Bar
 Progress Bar
 Critical Activity

L08F

LM HOLDINGS, LLC

Central Cohasset Wastewater PH IV

Revised BASELINE SCHEDULE


Sheet 1 of 5

NOTE 1: Water By-pass & Watermain Installation will be Interrupted During Winter Months.




NOTE 2: Any Waterwork not Finished This Fall Will Be Pushd Into the Spring



Activity ID	Orig Dur	Rem Dur	Cal ID	Early Start	Early Finish	Total Float	2007												2008												2009											
							J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	E					



Start Date 11JUL07
 Finish Date 05AUG09
 Data Date 19OCT07
 Run Date 26OCT07 12:27

 Early Bar
 Progress Bar
 Critical Activity

L08F
 LM HOLDINGS, LLC
 Central Cohasset Wastewater PH IV
 Revised BASELINE SCHEDULE

Sheet 5 of 5
 NOTE 1: Water By-pass & Watermain Installation will be Interrupted During Winter Months.
 NOTE 2: Any Waterwork not Finished This Fall Will Be Pushd Into the Spring

